

Work Order ID 155886***155886***

Page 1

Wednesday, January 18, 2017 7:34:59 AM

Item ID: D4961-041 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Tube Assembly
Start Date: 1/30/2017 Start Qty: 4.00 ***4*** Cust Item ID:
Required Date: 2/1/2017 Req'd Qty: 4.00 ***4*** Customer:
Reference:

Approvals: Process Plan: **DAS 21 9-89** Date: JAN 20 2017 Tooling: Date: Run Start ***NR1***
QC: Date: SPC (Y/N): Date: Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D4961	C

110

0.00

110

Small Fab

Memo

0.29

Small Fab

1- Cut D4961-1 tube to size as per dwg

2- On one side of tube flare end as per dwg then slide sleeves and nuts, flare other side of tube as per dwg.

4 0 17-1-26 **DAS 19 9-89**

120

QC5- Inspect part completeness to step on W/O

0.00

120

QC

Memo

0.01

Quality Control

4 **DAS 38 9-89**
JAN 27 2017

130

Identify as per dwg & Stock Location: **S+139**

0.00

130

Packaging

Memo

0.01

Packaging

DAS 21 9-89
JAN 30 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : _____					

Work Order ID 155886

Wednesday, January 18, 2017 7:34:59 AM

155886

Page 2

Item ID: D4961-041 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Tube Assembly
Start Date: 1/30/2017 Start Qty: 4.00 ***4*** Cust Item ID:
Required Date: 2/1/2017 Req'd Qty: 4.00 ***4*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.07							
Quality Control									

17/01/30 *MF*
17-1-30

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval																																																									
Description Work Order Deviation				Disposition				Completed By																																																									
								Lead hand / Supervisor Approval Verification																																																									
								QC / QA Coordinator Approval																																																									
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____			
Misidentified ☐	Past Due ☐																																																																

Picklist Print

Tuesday, January 17, 2017 1:56:58 PM

Page 1

Work Order ID: 155886

155886

Parent Item: D4961-041

D4961-041

Parent Item Name: Tube Assembly

Start Date: 1/30/2017

Required Date: 2/1/2017

Start Qty: 4.00

Required Qty: 4.00

Comments: IPP REV:A 13.10.22 NEW ISSUE DD VERF:JFS IPP
REV:B 15.02.18 AS PER DWG REV.B DD VERF:JFS

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

AN818-L12J		Purchased		No		110	Each	16.0000	2	8			
------------	--	-----------	--	----	--	-----	------	---------	---	---	--	--	--

AN818-L 12.J

Nut

**

17-1-26

DAS
19
9-89

Location	Loc Qty	Loc Code
OVER007	16	
M135704	6	
M135979	10	

M304TR0.750W.049		Purchased		No		110	f	89.7292	0.7	2.947368			
------------------	--	-----------	--	----	--	-----	---	---------	-----	----------	--	--	--

M304TR0 750W 049

304 RD Tube .750 x .049W

**

17-1-26

DAS
19
9-89

Location	Loc Qty	Loc Code
GA002	89.7292251	
M134528	30.2105266	
M134824	4.8478935	
M135093	1.905367	
M135242	26.0494815	
M135373	26.590643	
M135709	0.0790537	
M135857	0.0003668	
M136323	0.045893	

MS20819-12J		Purchased		No		110	Each	18.0000	2	8			
-------------	--	-----------	--	----	--	-----	------	---------	---	---	--	--	--

MS20819-12.J

Sleeve

**

17-1-26

DAS
19
9-89

Location	Loc Qty	Loc Code
ST305	18	
m135704	8	
m135979	10	

4
4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐



Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
3AC 81 88-2 3AC 81 88-2									

Root Cause				FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		
OTHER : _____							

ITEM	QTY	P/N	DESCRIPTION
	X	D4961-041	TUBE ASSEMBLY
1	1	D4961-1	TUBE
2	2	AN818-L12J	NUT, TUBE COUPLING (DRILLED)
3	2	MS20819-12J	SLEEVE

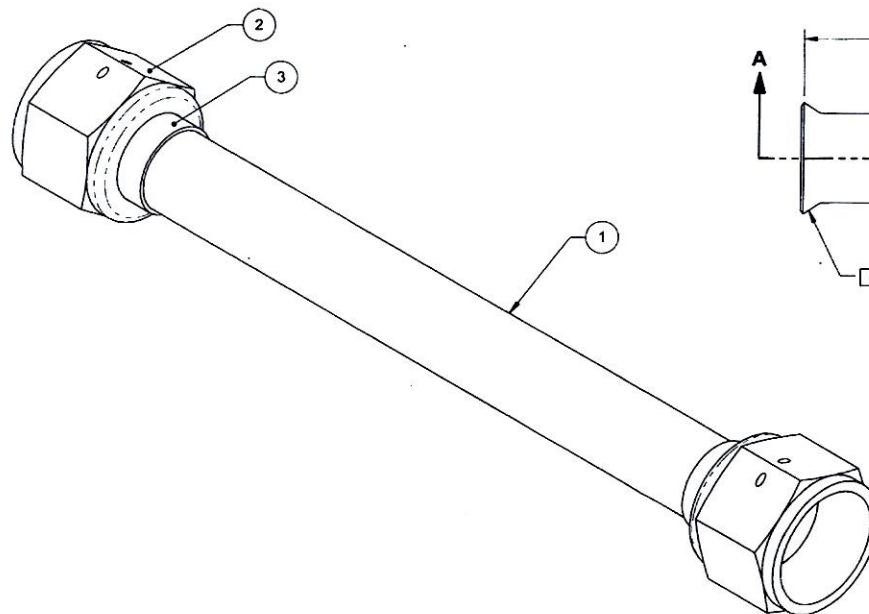

D4961-041 TUBE ASSEMBLY

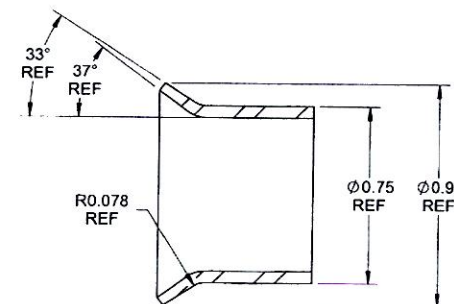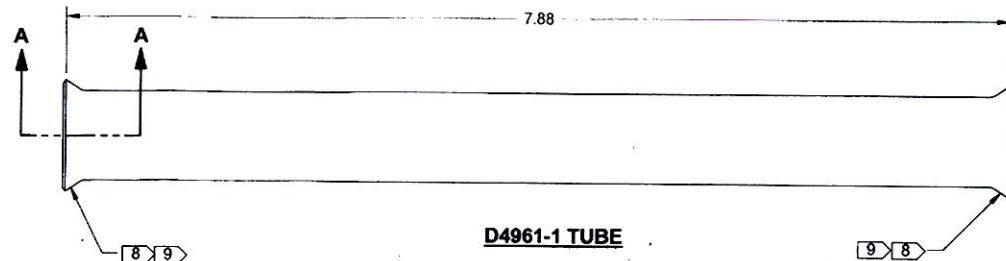

- NOTES:**
- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SEAMLESS ROUND TUBING, $\phi 0.750 \times 0.049$ WALL PER ASTM A213 OR ASME SA213 OR ASTM A269 (REF DART SPEC M304TR)
 - 2) FINISH: N/A
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: IDENTIFY PER QSI 044 6.1
 - 7) WEIGHT: 0.59 lbs
 - 8) FLARE TUBE PER MS33584
 - 9) CLEAN INSIDE OF TUBE AFTER FLARING ENDS

RELEASED
2016-08-04
ECW 16-622

APPROVED

C	ADDED D4961-045 (SHEET 3)	CC	16.06.21
B	UPDATED BOM P/N AN818-L12J WAS AN818-12J. ADDED SHEET 2 (D4961-043)	AK	14.11.07
A	NEW ISSUE	VS	13.10.21
REV.	DESCRIPTION	BY	DATE
DESIGN	VS		
DRAWN	CC		
CHECKED	VS		
MFG. APPR.	DD		
APPROVED	HS		
DE APPR.	DS		
DATE	16.06.21		

DART AEROSPACE LTD
HAWKESBURY, ONTARIO, CANADA

DRAWING NO.
D4961

TITLE
TUBE ASSEMBLY

REV. C
SHEET 1 OF 3
SCALE
NTS

COPYRIGHT © 2016 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE, OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.
